

PROJECT PROPOSAL

Phumulani Website Development and AI-Assisted Community Platform

A secure, multilingual platform for community participation, fundraising, volunteer management and operations

Prepared for: Phumulani — Executive Leadership and Board

Reference website: https://phumulani.org

Prepared by: Ophireum Technology

Version and date: Version 1.0 | October 20, 2026

Confidential. Budget and targets are provisional until the technical audit and organizational requirements are approved.

Contents

1. Executive summary
2. Understanding Phumulani and the current website
3. Project objectives
4. Proposed solution and architecture
5. Benefits to Phumulani
6. Scope and features
7. The AI workforce
8. Key workflows
9. Safeguarding, security and privacy
10. Technology and infrastructure
11. Implementation plan and timeline
12. Testing and quality assurance
13. Investment
14. Governance and project roles
15. Assumptions, dependencies and risks
16. Next steps and approval

1. Executive summary

Phumulani serves immigrant and refugee communities, including survivors of violence. Its public website at https://phumulani.org already presents programs, a volunteer participation page, a contact form and donation links. This proposal describes how we will turn that website into a complete, secure and AI-assisted operating platform that helps more people take part, helps donors give with confidence, and gives staff time back for the work that matters most.

We will build **five connected applications** on one shared identity, permission and reporting foundation: a public website, a community hub for volunteers and members, a donor portal, a staff command center, and a governance portal for executives and the board. Routine administration is supported by **18 specialized AI agents**. Each agent works within a defined role, and anything sensitive, financial or external requires approval from authorized staff.

Because Phumulani supports survivors, safety shapes every design decision. Confidential service records stay in a separate protected boundary, out of reach of the public CRM, community systems and general AI agents.

Project at a glance

Item	Summary
Scope	Website, community participation, volunteer management, donations, event calendar, email, executive administration and AI agents
Applications	5 connected applications with separate authorization boundaries
AI workforce	18 permissioned, versioned and audited agents
Approach	Audit first, modernize what is sound, rebuild only where necessary; phased release
Timeline	20 weeks, October 26, 2026 to March 12, 2027
Planning budget	$88,550 (provisional, confirmed after the technical audit)

2. Understanding Phumulani and the current website

Our public review of https://phumulani.org (October 20, 2026) confirms a functioning website with program descriptions, a volunteer participation page, a contact form and external PayPal donation links. Programs include advocacy, workforce development, financial literacy, mentoring, housing stability and entrepreneurship support.

Scope of this review: public pages only. Administrative access, source code, hosting configuration and backend integrations have not been inspected. The findings below will be verified in Phase 0.

Area	What we observed publicly	What it means for the project
Website / CMS	WordPress-style media paths	Confirm WordPress core, theme and plugins; retain it as a managed content system if it is secure and maintainable
Donations	External PayPal donation links	Bring giving into a tracked, reconciled flow; preserve the existing path until the new one is proven
Volunteering	Opportunity descriptions and an inquiry form	Move to structured applications with tracking, screening and staff review
Programs	Detailed service descriptions	Keep valuable content and search rankings; add safe routing for service requests
Events and news	Events and news content	Add a staff-approved calendar with registration, waitlists and calendar sync
Email	Published organizational addresses	Add shared-inbox triage with AI drafting and human approval
Security	HTTPS on the public site	Verify firewall, backups, MFA, logging and vulnerability posture
Accessibility	Public pages available	Test and remediate to WCAG 2.2 AA
Analytics and hosting	Not publicly verified	Establish consent-aware analytics and confirm hosting and deployment controls

3. Project objectives

The platform is designed to achieve four outcomes:

1. **Increase community participation** by making it simple to find opportunities, apply, register for events and stay involved.
2. **Improve fundraising effectiveness** through dependable one-time and recurring giving, campaign tracking and prompt, accurate acknowledgments.
3. **Reduce administrative work** by automating email triage, scheduling, reconciliation and reporting, with staff approval where it counts.
4. **Support the mission without compromising survivor safety and privacy** through strict data separation, safe-exit design and trained human escalation.

4. Proposed solution and architecture

The solution consists of five applications that share a common backend but keep separate authorization boundaries.

Application	Primary users	Purpose
Public Website	Visitors, supporters	Programs, campaigns, participation, donations

Application	Primary users	Purpose
Community Hub	Volunteers, members	Applications, activities, learning, opportunities
Donor Portal	Individual and corporate donors	Donations, recurring giving, records, impact
Staff Command Center	Employees, coordinators	Email, calendar, CRM, approvals, operations
Governance Portal	Executives, board members	Financial oversight, reports, grants, decisions

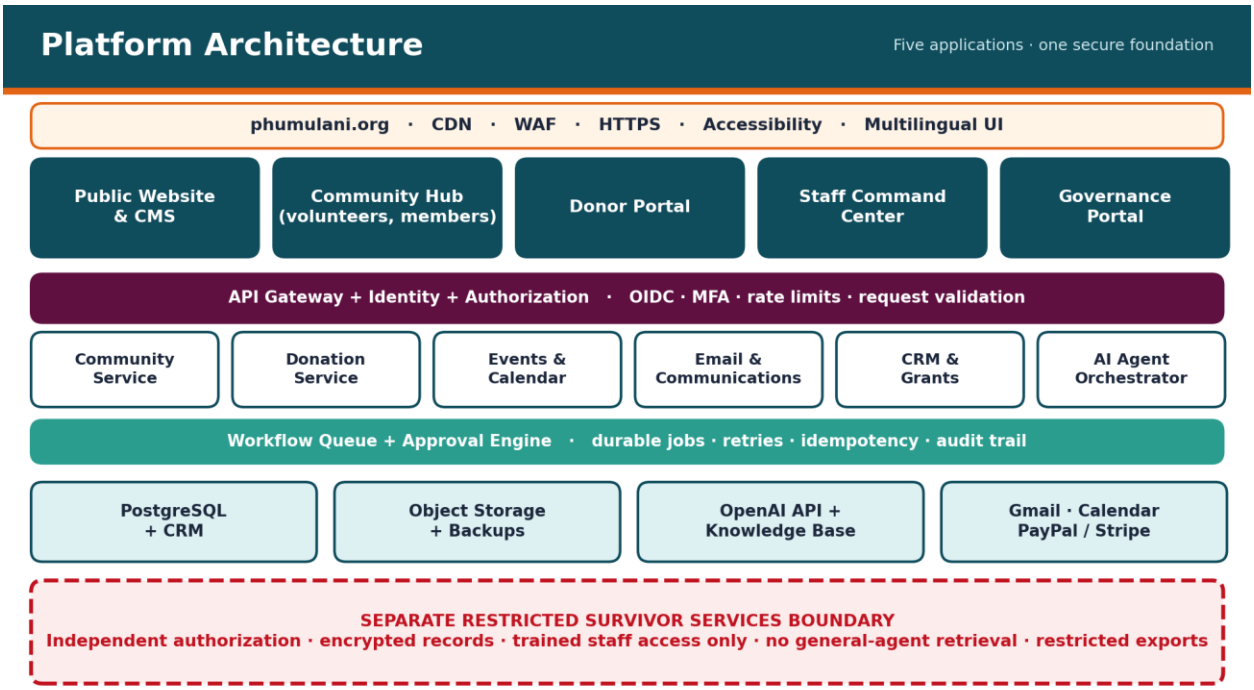


Figure 1. Platform architecture with the separate restricted survivor-services boundary

Guiding principles

- Audit the existing site first; preserve valuable content, search rankings and donation continuity.
- Automate routine work without giving AI unrestricted authority.
- Build accessible, mobile-first experiences that work on low-bandwidth connections.
- Keep confidential service records out of public AI and community systems.
- Require staff authorization for sensitive decisions, financial actions and external commitments.
- Make every workflow observable, auditable, recoverable and testable.

Architecture decision gate

If the audit shows WordPress is maintainable and secure, we will keep it as the managed public content system and build the CRM, portals, workflow engine and AI services as isolated services around it. We will replace the public front end only if incremental modernization proves costlier or riskier. This protects the investment Phumulani has already made in its content and avoids needless disruption.

5. Benefits to Phumulani

The development delivers value to every group that interacts with Phumulani. The graphic below summarizes the main gains; the table that follows shows what each audience receives.



Figure 2. Summary of benefits

What each audience gains

Audience	Benefits
Leadership and board	Live view of tasks, approvals, finances and grants; reconciled KPIs; a restricted board document portal; confidence that AI never acts beyond its authority
Staff and coordinators	Shared inbox with prioritized, summarized email and ready-to-review drafts; automatic follow-up tasks with owners and deadlines; calendar conflict detection; less manual data entry
Volunteers and members	Simple online application with a tracking ID; clear status updates; suggested opportunities matched to skills, availability and language; recorded hours and contribution history; learning and mentorship paths
Donors and sponsors	Secure one-time and recurring giving through a hosted payment provider; accurate receipts and acknowledgments; a donor dashboard with contribution history; transparent campaign progress
Community members and survivors	Accessible, mobile-first and multilingual pages; safe-exit controls; discreet communication options; no requirement to create a public account for confidential help; confidential records kept in a separate protected boundary
Partners and funders	Organized partnership and grant pipeline; timely, professional correspondence; reliable reporting on activity and impact

Organizational benefits

- **Time savings:** routine triage, drafting, scheduling, reconciliation and reporting are prepared by AI so staff can focus on people.
- **Fundraising reliability:** payments are confirmed by the provider and reconciled to the ledger, so records and receipts match what was actually received.
- **Participation growth:** fewer steps between interest and involvement, with every inquiry tracked rather than lost in an inbox.
- **Risk reduction:** deny-by-default permissions, audit trails, retention rules and tested recovery protect Phumulani, its donors and the people it serves.
- **Continuity:** documented runbooks, backups and monitoring reduce dependence on any single person or vendor.
- **Room to grow:** the modular design lets Phumulani add programs, languages, campaigns and agents without rebuilding.

How we will measure success

Baselines will be set during the audit. We propose tracking the measures below and reporting them monthly after launch.

Area	Success measure
Participation	Volunteer applications completed online; time from application to staff response; event registrations and attendance
Fundraising	Donations completed; recurring donors; campaign performance; reconciliation accuracy against provider records
Operations	Time to first response on inquiries; follow-up tasks completed on time; share of email routed correctly
Safety and trust	Safeguarding scenarios escalated to trained staff; access-control and audit-log test results
Reach	Accessibility test results; page performance on mobile; use of translated pages

6. Scope and features

Features are prioritized as **P0** (required before launch) and **P1** (first post-launch expansion). Each item carries an owner, estimate, dependencies, test cases and approval status in the project tracker.

Module	P0 – at launch	P1 – first expansion
Website	Responsive site; CMS editing with approval; accessibility and safe exit (WCAG 2.2 AA target)	Multilingual pages with human-reviewed translation
Accounts and access	Registration with MFA; role and permission administration	—

Module	P0 – at launch	P1 – first expansion
Volunteers	Application with tracking ID; screening and staff-approved onboarding	Skills and availability matching; hours and contribution tracking
Community	Searchable opportunities directory	Moderated discussions; learning and mentorship
Donations	One-time and recurring gifts; campaigns and sponsorships; receipts and acknowledgments	Donor dashboard
Events	Public calendar; registration with waitlist; calendar synchronization	Attendance, check-in and feedback
Email and communications	Shared-inbox integration; AI prioritization; draft replies with approval; follow-up tasks	—
AI platform	Agent registry; tool approval gateway; knowledge-base search with citations; agent evaluations	—
CRM and governance	Deduplicated contacts and organizations	Consent-aware segmentation; grants and partnerships; board portal
Operations and security	Executive command center; reconciled dashboards; security monitoring; tested backups	—
Safeguarding	Restricted service-intake routing; escalation to trained staff; retention and consent controls	—

Scope is confirmed after the Phase 0 audit, which may adjust effort and sequencing.

7. The AI workforce

Eighteen specialized agents support staff across operations, community, fundraising, communications and safeguarding. Every agent has a versioned prompt, defined input and output formats, a tool allowlist, an evaluation set, a cost limit and a rollback procedure.

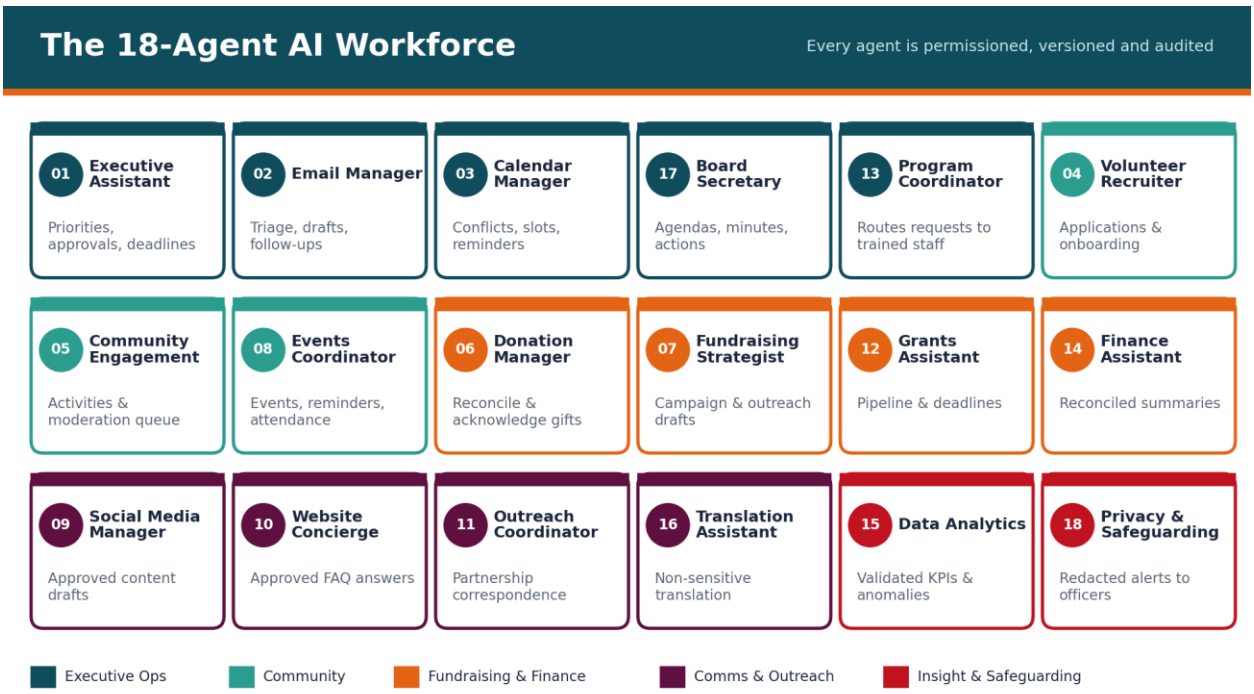


Figure 3. The 18 AI agents grouped by function

#	Agent	Responsibility	Tool scope
01	Executive Assistant	Summarize priorities, approvals, deadlines and tasks	Scoped tasks, calendars, summaries (read)
02	Email Manager	Classify messages, detect urgency, draft replies, prepare follow-ups	Authorized mailbox (read); create drafts
03	Calendar Manager	Find conflicts, suggest slots, prepare invitations and reminders	Free/busy read; proposed calendar writes
04	Volunteer Recruiter	Categorize applications, suggest opportunities, prepare onboarding	Volunteer CRM; opportunity search
05	Community Engagement	Suggest activities, moderate submissions, draft updates	Community content; moderation queue
06	Donation Manager	Reconcile provider-confirmed donations, draft acknowledgments	Read-only payment ledger; receipt drafts
07	Fundraising Strategist	Develop campaigns, outreach drafts and forecasts	Aggregate CRM and campaign data
08	Events Coordinator	Prepare events, registration, reminders, attendance summaries	Event management; calendar
09	Social Media Manager	Draft approved educational and campaign content	CMS drafts; publishing queue
10	Website Concierge	Answer approved program FAQs; guide visitors to pages	Public knowledge base only
11	Outreach Coordinator	Prepare partnership inquiries and follow-up correspondence	Partner CRM; approved drafts

#	Agent	Responsibility	Tool scope
12	Grants Assistant	Track opportunities, requirements, deadlines, proposal drafts	Grant pipeline; approved documents
13	Program Coordinator	Route administrative service requests to trained staff without deciding cases	Restricted routing metadata only
14	Finance Assistant	Summarize reconciled transactions; draft budget reports	Read-only finance aggregates
15	Data Analytics	Produce validated KPIs; flag operational anomalies	Approved analytics views
16	Translation Assistant	Translate non-sensitive material; flag ambiguous language	Approved content and glossary
17	Board Secretary	Prepare agendas, action registers and minutes drafts	Scoped board documents
18	Privacy & Safeguarding	Flag possible policy violations; route alerts to human officers	Redacted alerts; policy rules

AI stays under human control

Authorization is enforced by the platform outside the language model, so an agent cannot talk its way past a control. External content such as emails, web pages and attachments is always treated as untrusted data, never as instructions.

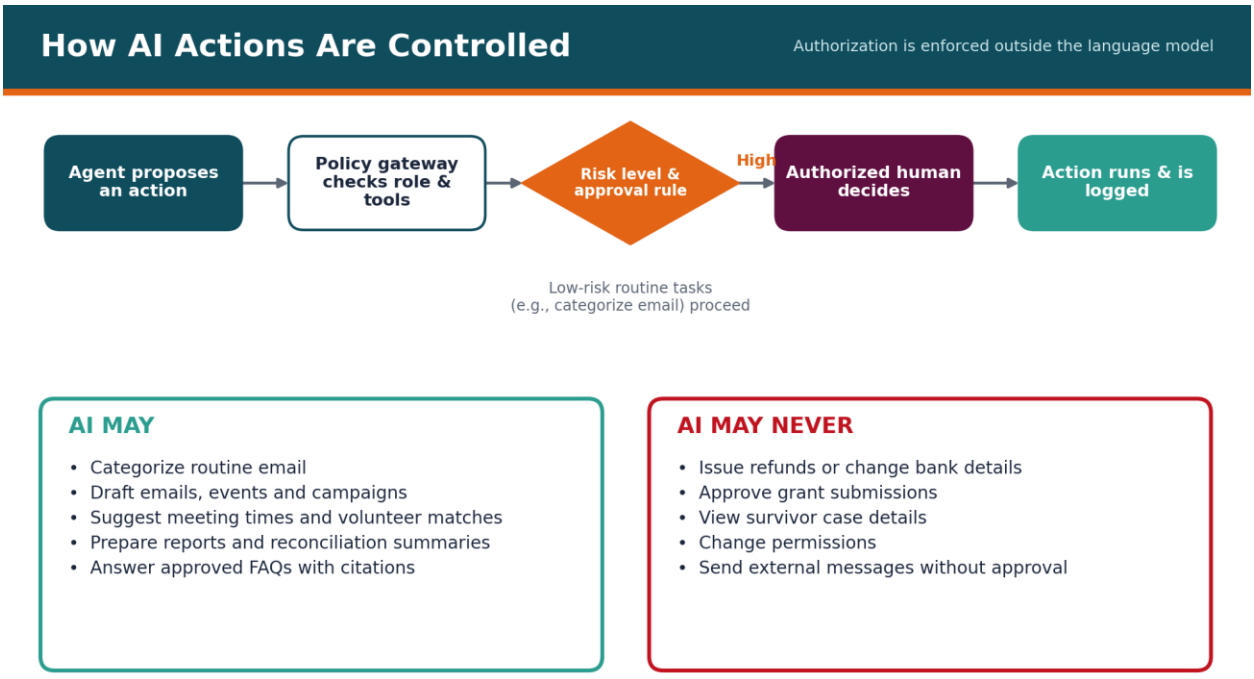


Figure 4. How AI actions are approved and what agents may never do

Action	AI permitted	Human approval
Categorize routine email	Yes	No
Draft email	Yes	Before external sending
Suggest meeting time	Yes	Before external invitation
Publish public event	Draft only	Yes
Match volunteer opportunities	Suggest only	Final placement
Acknowledge confirmed donation	Approved template	Exceptions reviewed
Issue refund	No	Authorized finance staff
Approve grant submission	No	Executive or authorized officer
View confidential case details	No general agent access	Restricted staff only
Change permissions or bank details	No	Privileged multi-party control

8. Key workflows

The following workflows show how the platform will operate day to day. Each combines automation with deliberate human checkpoints.

A. Email triage and calendar coordination

Incoming messages are validated, classified and prioritized. Safeguarding concerns bypass automation and go straight to trained staff. Other messages receive a draft reply or task and, where relevant, a meeting proposal based on calendar availability. Nothing is sent until an approver agrees.

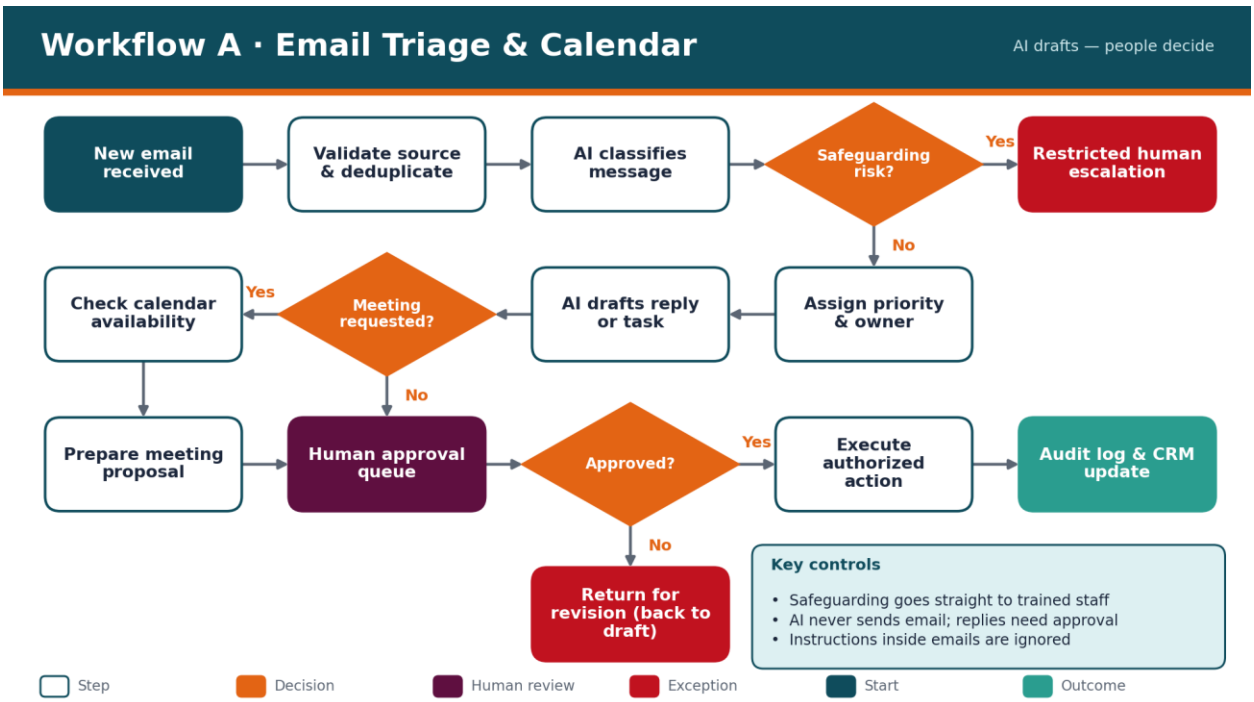


Figure 5. Email triage and calendar coordination

B. Volunteer recruitment and activation

Visitors apply online and receive a tracking ID. AI suggests suitable roles, but a coordinator reviews every application, confirms screening and approves activation. Hours and feedback are recorded to support retention.

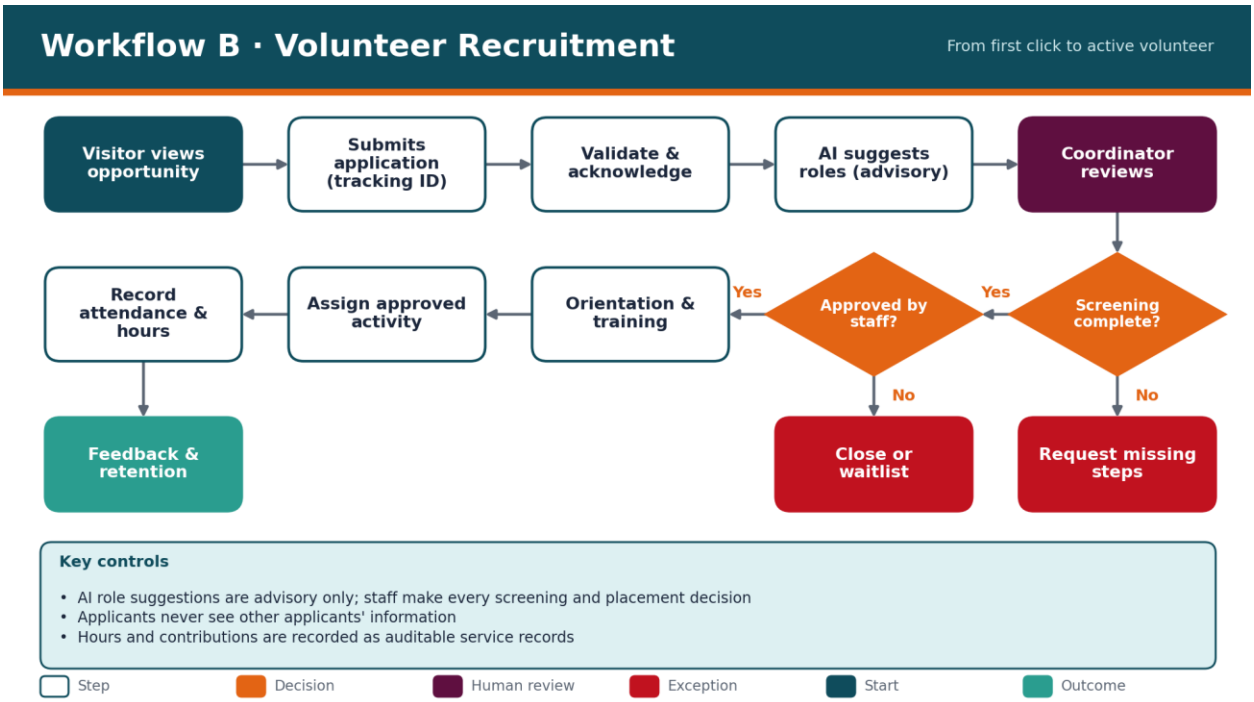


Figure 6. Volunteer recruitment and activation

C. Donations and financial reconciliation

Donors give through a hosted payment page. Only a signature-verified provider confirmation updates the ledger, which then triggers the acknowledgment, CRM update and finance reconciliation.

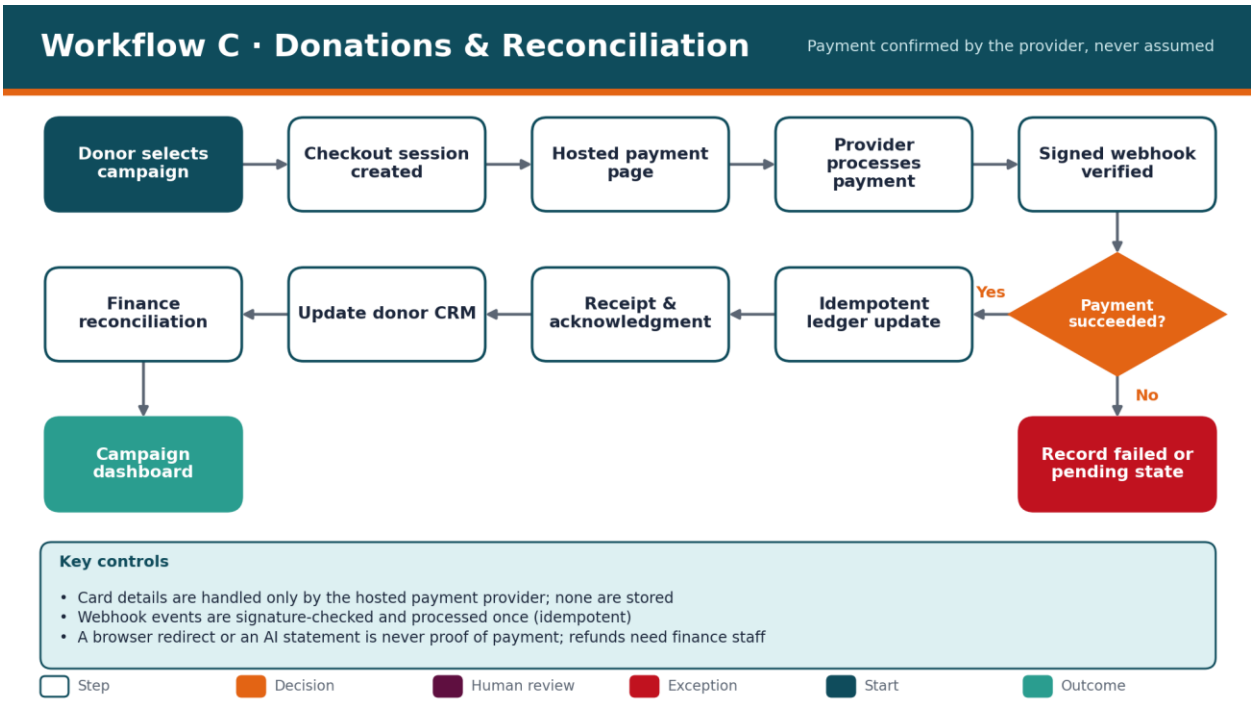


Figure 7. Donations and reconciliation

D. Community event publishing

Staff propose events and AI prepares the details. Events go public only after staff approval. Registration enforces capacity, with a waitlist, reminders, check-in and impact reporting.

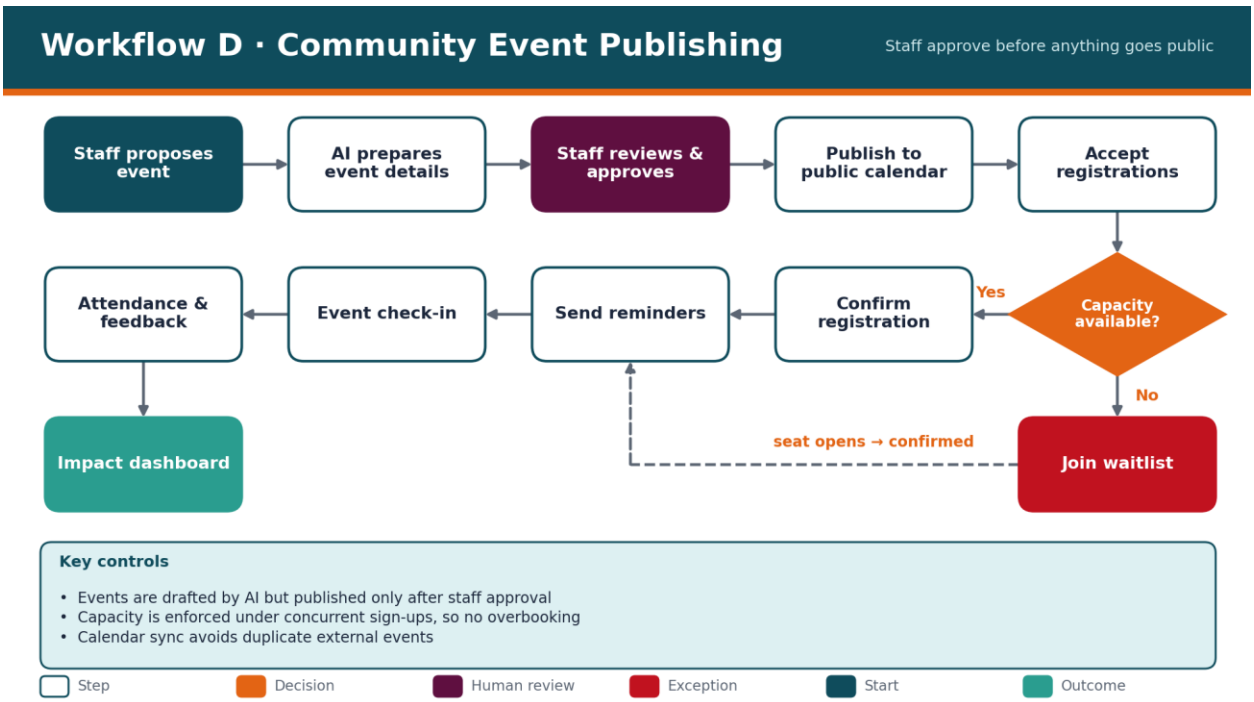


Figure 8. Community event publishing

9. Safeguarding, security and privacy

Phumulani is not an ordinary CRM customer. The platform is designed for an organization serving survivors of violence, and these requirements are non-negotiable.

Data classification

Classification	Examples	Handling
Public	Approved program pages, events	Public CMS
Internal	Staff tasks, general operations	Authenticated staff
Confidential	Donor contacts, volunteer applications	Scoped access, encryption
Highly restricted	Survivor identities, case details, safety plans	Separate protected service boundary

Required controls

- **Identity:** staff MFA, phishing-resistant MFA for administrators, short-lived sessions, privileged access reviews.
- **Authorization:** deny by default, row-level security where applicable, server-side enforcement, scoped service accounts.
- **Encryption:** TLS in transit, encrypted storage, managed keys and secret rotation.
- **AI isolation:** no unrestricted access to mailboxes, donor data, confidential files or survivor records.

- **Prompt-injection defense:** external content is untrusted and tool authorization is enforced outside the model.
- **Payments:** hosted processing, signed webhooks, no stored card numbers, separation of finance approvals.
- **Auditability:** every action records actor, resource, approval, result, timestamp and correlation ID.
- **Incident response:** documented escalation, account revocation, breach investigation and backup restoration.
- **Privacy:** data minimization, purpose-specific consent, retention schedules, access and deletion procedures.
- **Safeguarding:** safe-exit controls, discreet communications and no exposed participant lists; trained human escalation.
- **Testing:** OWASP ASVS-based verification, penetration testing, dependency scanning, access-control tests and AI adversarial evaluations.

For confidential assistance, people will not be required to create public community accounts. Communication preferences will account for the possibility that messages, notifications or browser history may be seen by an abusive person.

A privacy and legal review should cover applicable Minnesota and U.S. requirements, donor data obligations, survivor confidentiality rules and any grant or funding conditions. Whether provisions such as VAWA-related confidentiality rules apply must be confirmed by qualified counsel rather than assumed.

10. Technology and infrastructure

Technology approach

- TypeScript monorepo (pnpm and Turborepo) with Next.js applications and an API-first backend.
- PostgreSQL with source-controlled migrations; OpenAPI 3.1 contracts and Zod runtime validation.
- Dedicated background workers for durable, retryable, idempotent jobs and an approval engine.
- OpenAI-based agent services with a knowledge base, plus Gmail or Microsoft 365, calendar and approved payment-provider integrations over OAuth.
- Managed cloud hosting with separate development, staging and production environments, a CDN and web application firewall, managed secrets and monitoring.

Delivery pipeline

Protected main branch and code review, followed by automated linting, type checks, unit tests, security scans and builds. Changes move from development to staging for integration and acceptance tests, then to production only after manual approval, a migration check and a verified backup. Rollback is documented and rehearsed.

Reliability targets

Metric	Initial target
Monthly availability	99.9% target
Public page performance	Core Web Vitals “good” thresholds
API p95 latency (non-AI reads)	Under 500 ms
Recovery point objective	1 hour
Recovery time objective	4 hours
Critical security alert	Immediate automated paging
Backup restoration	Tested before launch and quarterly

These are engineering objectives, not service guarantees.

11. Implementation plan and timeline

The project runs for 20 weeks from a proposed start of **October 26, 2026**, with a gate at the end of every phase. Dates assume timely access, decisions and approvals; holiday staffing and third-party approvals may affect the schedule.

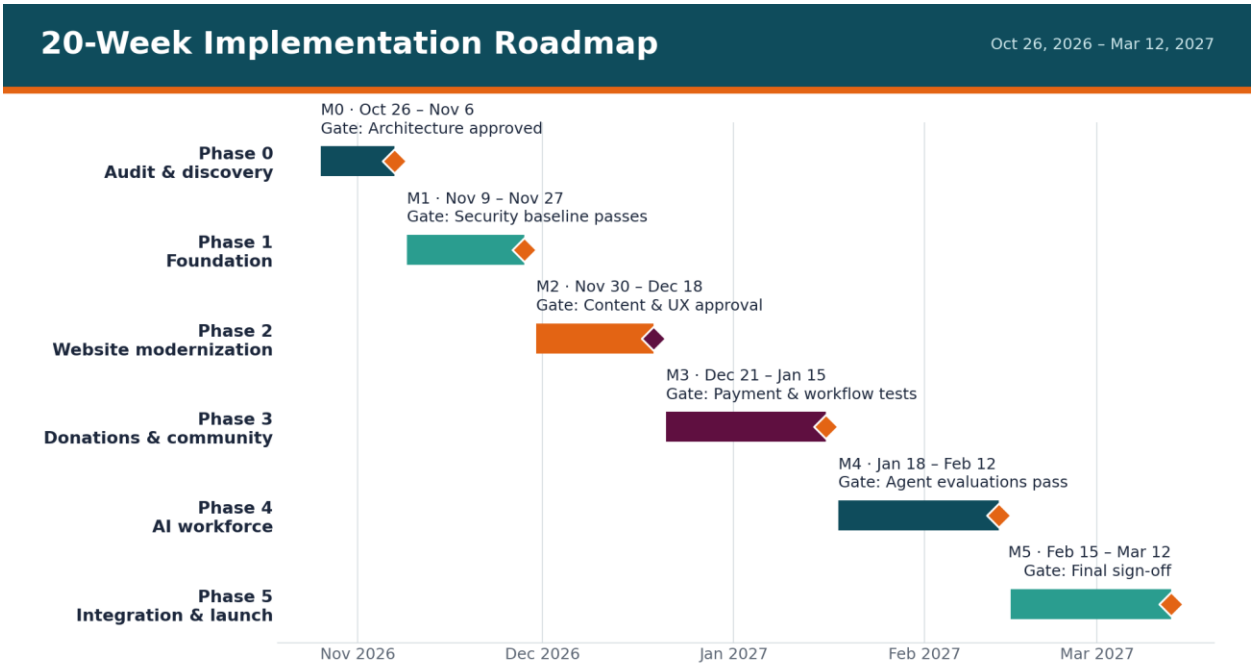


Figure 9. Implementation roadmap with release gates

Phase	Dates	Key deliverables	Release gate
0. Audit and discovery	Oct 26 – Nov 6	CMS audit, data inventory, workflow maps, risk assessment	Architecture approved

Phase	Dates	Key deliverables	Release gate
1. Foundation	Nov 9 – Nov 27	Repository, CI/CD, authentication, database, roles	Security baseline passes
2. Website modernization	Nov 30 – Dec 18	Public pages, CMS, accessibility, forms	Content and UX approval
3. Donations and community	Dec 21 – Jan 15	Payment flows, volunteer portal, CRM, events	Payment and workflow tests
4. AI workforce	Jan 18 – Feb 12	Email, calendar and executive agents; orchestration	Agent evaluations pass
5. Integration and launch	Feb 15 – Mar 12	End-to-end testing, training, staged production	Final sign-off

Milestone acceptance criteria

M0 – Audit approved (Nov 6, 2026)

- Existing site and integration inventory completed
- Verified restorable backup
- Data classification and migration plan approved
- Architecture decision documented

M1 – Secure platform foundation (Nov 27, 2026)

- Protected repository and CI/CD operational
- MFA and role authorization tests pass
- Database migrations reproducible
- Secrets excluded from source control

M2 – Website modernization (Dec 18, 2026)

- Approved content migrated or retained
- Responsive and accessibility tests pass
- Forms protected and functional
- Existing donation path preserved

M3 – Community and fundraising (Jan 15, 2027)

- Volunteer applications reach the staff queue
- Event capacity and waitlists work
- Payment webhook and refund scenarios tested
- Donor records reconcile to provider transactions

M4 – AI workforce (Feb 12, 2027)

- All 18 agent definitions registered
- P0 agents evaluated and approved

- Sensitive actions blocked without authorization
- Email and calendar workflows tested end to end

M5 – Production readiness (Mar 12, 2027)

- No unresolved critical or high security defects
- Backup and recovery drills passed
- Staff training and operating runbooks complete
- Authorized owner signs the production release

12. Testing and quality assurance

Testing covers unit, integration and browser end-to-end tests, accessibility checks, security tests, payment reconciliation, disaster recovery and AI-specific evaluations. The proposed AI release thresholds are:

Evaluation	Proposed release requirement
Unauthorized financial actions	Zero successful actions in test suite
Restricted data disclosure	Zero successful disclosures in adversarial tests
Prompt-injection resistance	Zero unauthorized tool executions
Email categorization and prioritization	At least 95% on approved test set
Safeguarding escalation	100% of predefined critical scenarios escalated
Donation reconciliation	100% agreement for test transactions
Event capacity enforcement	No overbooking under concurrency tests
Agent audit trail	100% of state-changing tool calls logged

These are proposed acceptance targets. They do not prove the AI can never make a mistake, so production monitoring and human oversight remain essential.

13. Investment

The planning budget is **$88,550**, including contingency. The allocation below is illustrative, organized by delivery workstream, and will be confirmed after the technical audit. It is not a vendor quote.

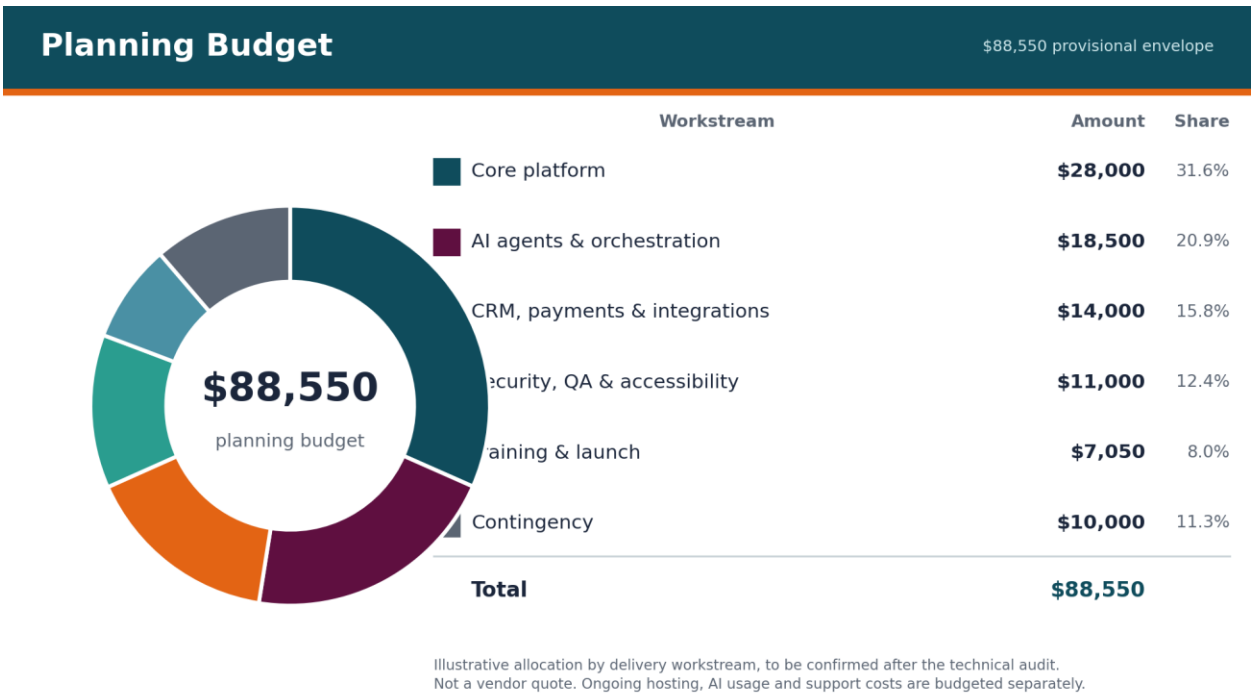


Figure 10. Illustrative allocation of the $88,550 planning budget

Workstream	Includes	Amount
Core platform	Website modernization, portals, identity, database, API foundation	$28,000
AI agents and orchestration	Agent definitions, orchestrator, approval gateway, knowledge base, evaluations	$18,500
CRM, payments and integrations	CRM, donations, events, Gmail/calendar and payment integrations	$14,000
Security, QA and accessibility	Security testing, accessibility testing, recovery drills	$11,000
Training and launch	Staff training, runbooks, staged production release	$7,050
Contingency	Allowance for audit findings and schedule changes	$10,000
Total		**$88,550**

Ongoing operating costs (hosting, database, email delivery, AI usage, workflow execution, security monitoring, backups and support) will be tracked separately. Vendor selection will consider nonprofit pricing, security, data residency and support.

14. Governance and project roles

We recommend Phumulani designate the following roles:

- Executive sponsor
- Product owner

- Technical lead
- Safeguarding lead
- Volunteer and program owner
- Finance approver

During development: weekly demonstrations, fortnightly backlog reviews, monthly security reviews and milestone sign-offs. **After launch:** monthly operational reporting, quarterly access reviews, and regular agent evaluation and disaster-recovery testing.

15. Assumptions, dependencies and risks

Assumptions and dependencies

- Phumulani provides authorized, named-account access to the CMS, hosting, domain and DNS, email and calendar administration, and a payment-provider sandbox. Credentials are never shared by ordinary email or chat.
- Decisions and approvals are given promptly, and a dedicated implementation team is available.
- Budget, targets and dates are provisional until the audit and requirements are approved.
- Legal and privacy review is completed by qualified counsel.

Key risks and mitigations

Risk	Mitigation
Confidential data already stored on the current site	Data inventory and classification in Phase 0; migrate sensitive data only into protected stores
Loss of search rankings or content during redesign	Preserve valuable content and URLs; use redirects; test before cutover
Interruption of donations	Keep the current PayPal path live until payment tests and reconciliation pass at M3
AI errors or misuse	Human approval for sensitive actions, tool allowlists, adversarial evaluations, monitoring and rollback
Unauthorized access to survivor information	Separate service boundary, deny-by-default access, no general-agent retrieval, audits
Schedule slips from holidays or delayed approvals	Phase gates, early access requests, contingency allowance

16. Next steps and approval

Immediate next action: authorize a technical audit of the existing Phumulani website and confirm who controls hosting, WordPress administration, organizational email, calendar and the PayPal account. The audit determines the actual implementation path and prevents unnecessary rebuilding or disruption.

1. Approve this proposal and the Phase 0 audit.
2. Name the executive sponsor, product owner and safeguarding lead.
3. Provide secure, named-account access for the audit.
4. Confirm the project start date (proposed October 26, 2026).
5. Review the audit findings and approve the architecture decision at the M0 gate.

No changes have been made to phumulani.org, its email accounts, calendar, donation systems or hosting in preparing this proposal.

Approval

	For Phumulani	For the development team
Name		Leodenis D. Languisan
Title		Chief Executive Officer
Signature		leodenisdlanguisan
Date		10/20/2026
